







WEST LINN - WILSONVILLE SCHOOL DISTRICT


2019 Capital Bond Program Quarterly Report

TABLE OF CONTENTS 02 2023

1.	2019 CAPITAL BOND PROGRAM SUMMARY	1
2.	PROGRAM MARKETING & PARTICIPATION	2
3.	PROJECT STATUS / SCHEDULES	
	ADDITION & RENOVATION @ WHS	3
	ATHEY CREEK MIDDLE SCHOOL @ DLR	6
	RIVERSIDE HIGH SCHOOL	9
	NEW PRIMARY SCHOOL @ FP	11
	LEARNING WITH TECHNOLOGY	13
	FACILITY IMPROVEMENTS	14

PROGRAM SUMMARY

Q2 2023

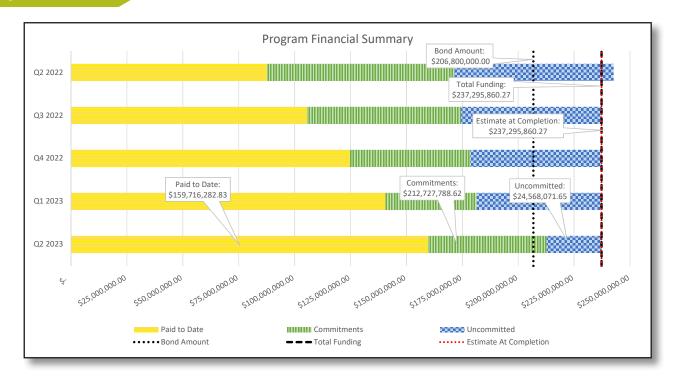

Bond Component	Original Budget	Approved Budget Changes	Current Budget	Current Commitments	Actuals Approved	Estimate At Completion	Forecasted Over/(Under)
Addition & Renovation @ WHS	28,470,000.00	9,873,063.38	38,343,063.38	37,148,926.24	35,274,737.42	38,343,063.38	0.00
New Middle School @ DLR	78,000,000.00	2,000,000.00	80,000,000.00	76,879,594.59	61,806,073.83	80,000,000.00	0.00
Riverside High School	11,673,000.00	3,555,022.25	15,228,022.25	14,572,819.97	12,039,373.34	15,228,022.25	0.00
Stadium & Parking @ WLHS	8,625,000.00	-655,343.86	7,969,656.14	7,969,656.14	7,967,378.47	7,969,656.14	0.00
New Primary School @ FP	39,000,000.00	5,999,537.22	44,999,537.22	35,467,628.53	7,432,049.19	44,999,537.22	0.00
Learning with Technology	15,000,000.00	-750,000.00	14,250,000.00	11,816,716.03	9,814,977.55	14,250,000.00	0.00
Facility Improvements	26,032,000.00	833,652.98	26,865,652.98	21,223,424.71	20,433,727.53	26,865,652.98	0.00
Subtotals	206,800,000.00	20,855,931.97	227,655,931.97	205,078,766.21	154,768,317.33	227,655,931.97	0.00
Program	20,139,622.10	-10,499,693.80	9,639,928.30	7,649,022.41	4,947,965.50	9,639,928.30	0.00
Grand Totals	226,939,622.10	10,356,238.17	237,295,860.27	212,727,788.62	159,716,282.83	237,295,860.27	0.00

Community members interested in keeping up with the bond program can sign up for for email updates through the District's ListServ system at: https://listserv.wlwv.k12.or.us/self-service/

- Over 89% of current funding, or \$212.7 million, has been committed
- Over \$19 million was spent this quarter for a total of \$159.7 million, over 67% of current funding
- The forecasted over/under for the program is balanced
- Program contingency transferred to support work at Wilsonville High School (\$600,000.00)
- Program contingency transferred to support work at Riverside High School (\$250,000.00)
- Financial data current as of July 12, 2023

PROGRAM MARKETING & PARTICIPATION 02 2023

Program Marketing:

The Bond Management Team built a program marketing plan to improve outreach to contractors, including minority and women-owned firms. The goal is to develop an extensive network of industry contacts that are kept informed of current and upcoming opportunities. A variety of platforms, both formal and informal, are being used to reach out and encourage all contractors that they are welcome, will be treated fairly, and can receive training on district-specific forms and processes.

The projects below represent over \$6.1 million dollars or just shy of 8% of minority-owned, disabled, veteran-owned womenowned or emerging small business contracts between four projects.

Inza Wood Middle School Project

- General Contractor: Inline Construction
- \$903.915 18.5% of the contract

New Athey Creek at Dollar Street Project

- General Contractor: Emerick Construction
- \$3.8 Million 6.2% of the contract

West Linn High School Stadium & Parking Project


- General Contractor: Par-Tech Construction
- \$1.3 Million 24.6% of the contract

Riverside High School Project

- General Contractor: Ross Builders
- \$133,323 2.1% of the contract

ADDITION & RENOVATION @ WHS

02 2023

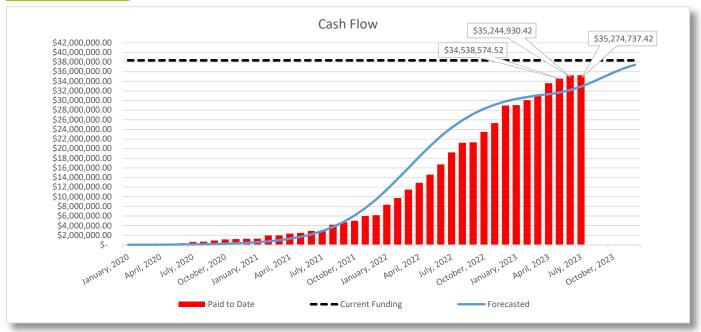

New 600 seat auditorium with supporting spaces to better accommodate growing school programs and support community performing arts. Also includes additional parking, site circulation improvements, synthetic turf softball field with sports field lights, and energy efficient lighting upgrades. Renovation of existing auditorium and black box theater spaces and conversion to classroom spaces including Career and Technical Education. Also includes safety & security upgrades, energy efficient lighting upgrades and mechanical equipment replacement.


Construction is expected to be phased from summer 2021 through summer 2023. The new auditorium is expected to open fall 2023. Renovated spaces are expected to open Fall 2023.

Recent Activities:

- Phase 4 is underway, which includes the Black Box and old theater converstion to CTE spaces
- Old auditorium in-fill is complete and structural work is underway
- Theater rigging systems inspections have been completed
- Required firewall work is currently underway
- Electrical rough-in has started in the new CTE spaces
- Final accoustical treatments have been installed
- Roof repairs have begun
- Final site plantings are underway

- Mechanical rough-in in the CTE space
- Stud framing work to begin on the new interior walls for the new CTE and Black Box spaces
- Installation of exterior building signage
- Additional mechanical screen wall work
- Existing exterior wall corrective work
- Final site work



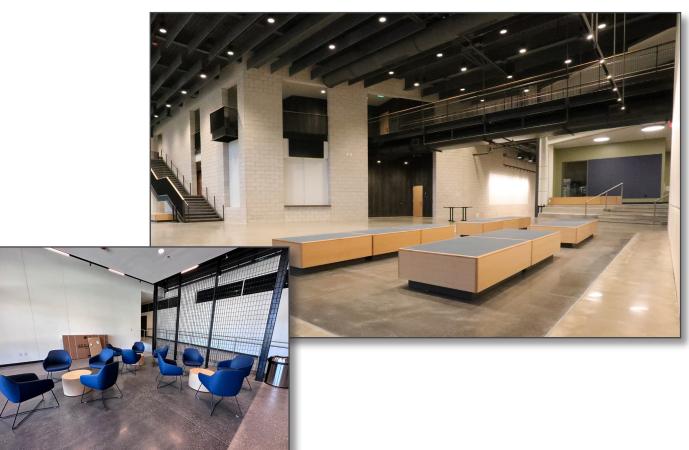






ATHEY CREEK MIDDLE SCHOOL @ DLR

02 2023

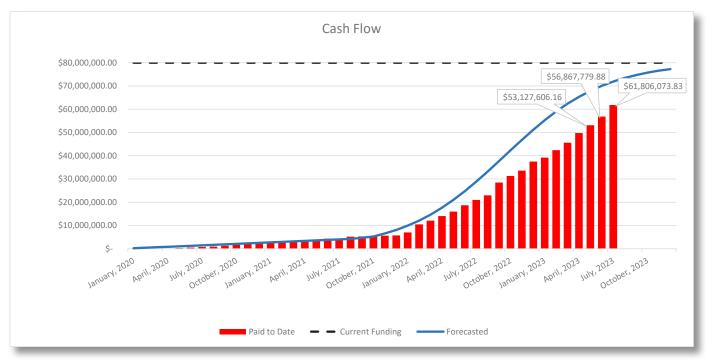

New 850 student middle school at the District's Dollar Street property to make Athey Creek Middle School a neighborhood school, and to provide a central location for Riverside High School.

Construction is expected early 2022 through summer 2023.

Recent Activities:


- Permanent power, water and networking are all up and running in the building
- Interior finishes are underway, including acoustic ceiling tiles, light fixtures, painting, tile and casework
- Large kitchen equipment is being installed including hood, walk in cooler and walk in freezer
- Theater equipment is being installed
- Elevator installation is complete
- Interior doors are being installed
- All Athey items have been moved out of the old building and into trailers until ready to go in the new space
- Final paving was completed on Dollar Street and staff parking lot
- The lower visitor parking lot and new driveway from Brandon Place were installed along with all sidewalks and striping. Parking lot islands are being irrigated and prepped for planting
- Brandon Place is paved.
- Exterior windows are nearly completed with the exception of the entry vestibules
- Solar array panels are installed on the upper level bus canopies
- Exterior light poles have been installed
- Both generators are installed and will begin testing
- The roof is complete and all but one rooftop unit is placed, with completion late July
- Landscaping has begun and will be ongoing throughout the summer months
- Fence installation has begun
- The concessions building is being constructed

ATHEY CREEK MIDDLE SCHOOL @ DLR Q2 2023

- Gym flooring is scheduled to start in July
- HVAC installation should be complete at the end of July and testing should begin in August
- Interior glazing will begin in July
- The track and field are being prepared for installation
- The playground equipment will be installed in the coming month
- Reconstruction of the West entry to Fields Bridge Park and construction of the roundabout is pending City of West Linn permitting
- Furniture arrives on site July 17th and will be installed over a two week period
- Movers will bring Athey Creek staff stored items to the site the first week of August
- Meeting with the City of West Linn to confirm temporary occupancy requirements
- Meeting with TVF&R to outline occupancy requirements
- Temporary entry constructed from Willamette Falls Drive




ATHEY CREEK MIDDLE SCHOOL @ DLR

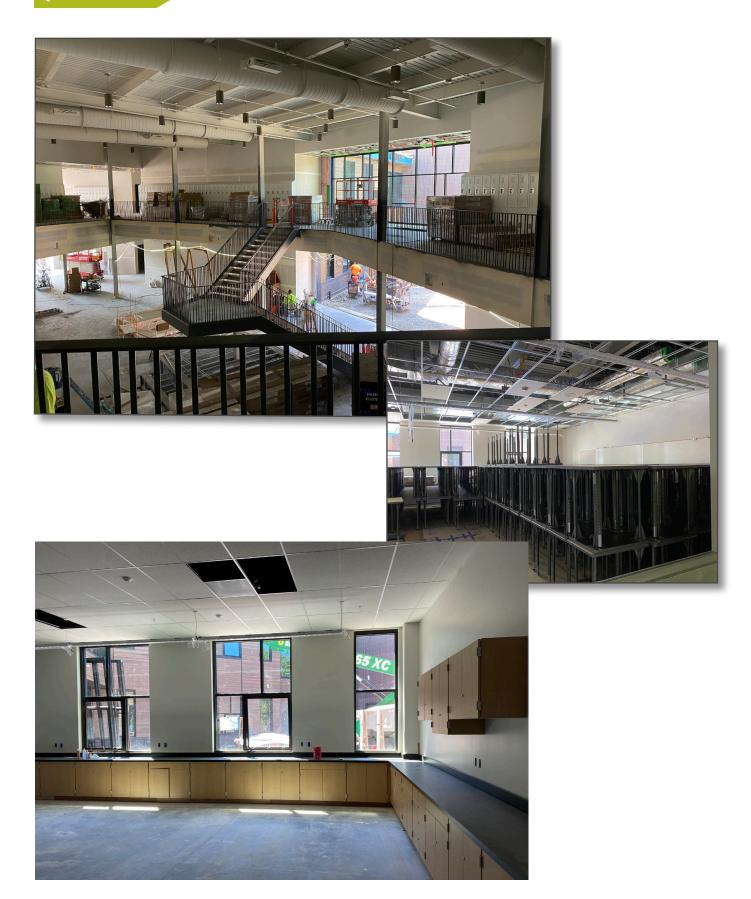

RIVERSIDE HIGH SCHOOL

02 2023

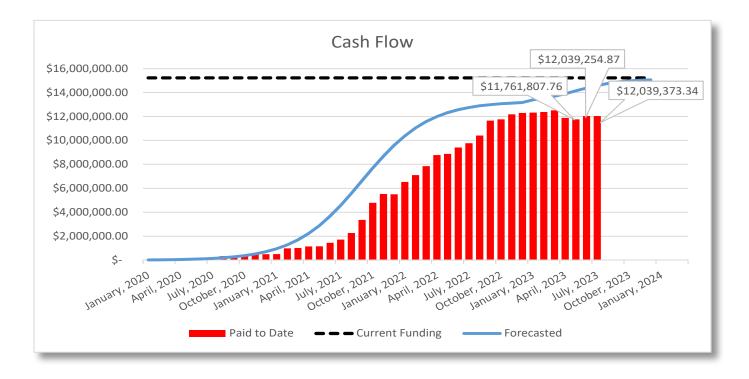

Office addition to accommodate Riverside High School and create a secure entry. Renovation of existing office space and conversion to classroom spaces, including Career and Technical Education. Also includes mechanical, electrical and plumbing upgrades, roofing replacement, and kitchen equipment upgrades.


Construction is expected summer 2021 through summer 2023.

Recent Activities:

- Final phase of conversion from Athey Creek Middle School to Riverside High School has begun
- Athey Creek materials have been removed from the building
- Demolition and site work is underway in the new CTE classroom spaces and outside the building
- Gym bleachers have been removed and salvaged for materials
- Furniture for the new Student Services Hub space has been delivered and assembled


- Installation of new gym bleachers, restriping and refinishing the gym floor to occur in August
- Rough-in of mechancial, electrical and plumbing in the CTE spaces
- Updating the library space with accoustical panels, paint and circulation desk
- New library, lobby, commons and select classroom furniture will arrive late July and early August

RIVERSIDE HIGH SCHOOL Q2 2023

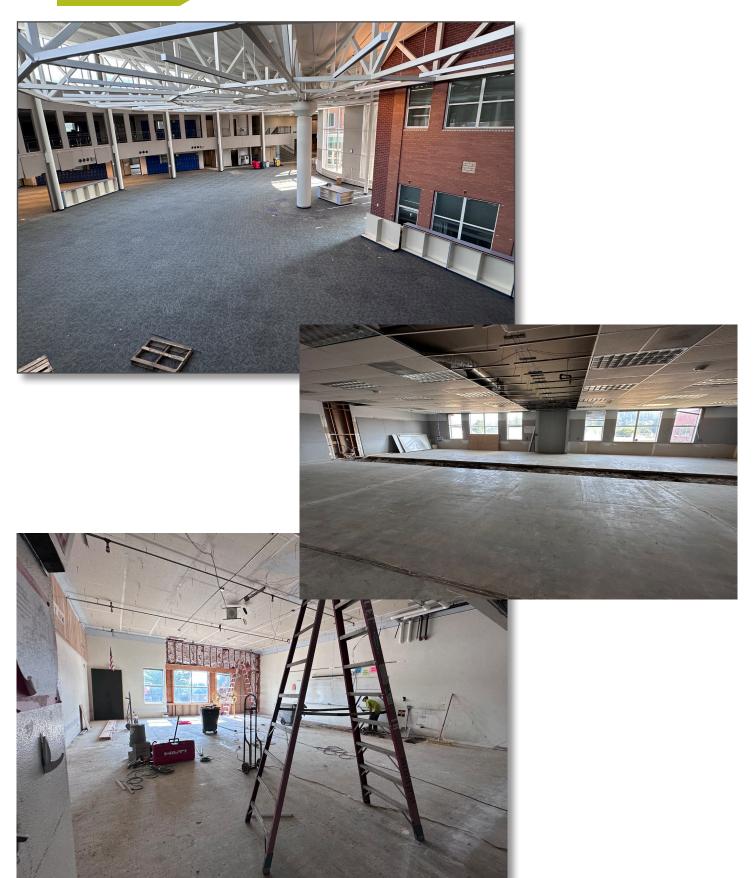

NEW PRIMARY SCHOOL @ FP

02 2023

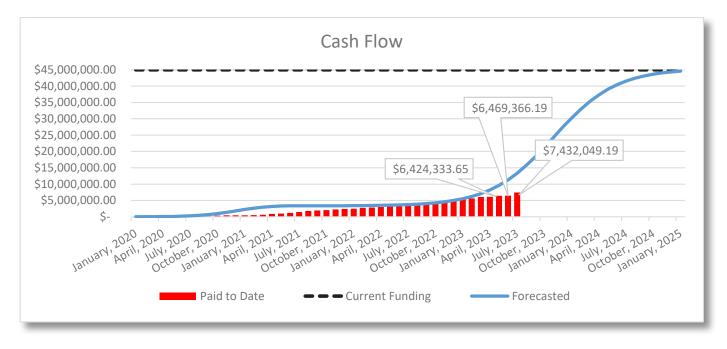

New 350 student starter primary school on the Frog Pond site to accommodate enrollment growth. New storage building to replace the storage being demolished at the new primary school site.

Construction of the District storage is complete.

Design of the primary school began in 2021.

Construction of the new primary school is expected summer 2023 through early 2025.

Recent Activities:


- Board approved contract with alternates
- Contract executed
- Abatement of existing buildings complete
- Contractor mobilized to the site

- Continued coordination between the City of Wilsonville and the District for the school work and the City's work on the Boeckman Road Corridor Improvements project
- Completion of erosion control and tree protection measures
- Start of construction





LEARNING WITH TECHNOLOGY Q2 2023

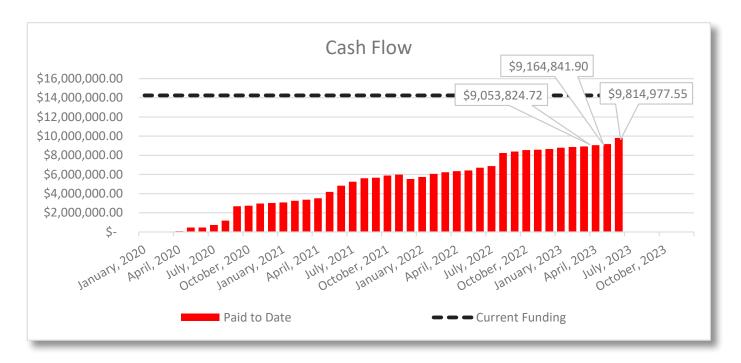

This project will roll out in phases across the District and include a wide array of infrastructure and devices that support student learning.


Recent Activities:

- Implementation of technology needs at new schools, Athey Creek and Riverside High
- Wifi updates
- Device replacements
- Digital display installations

- Implementation of technology needs at new schools, Athey Creek and Riverside High
- Acquisition of Chromebooks around the District
- Digital display installations

FACILITY IMPROVEMENTS

Q2 2023

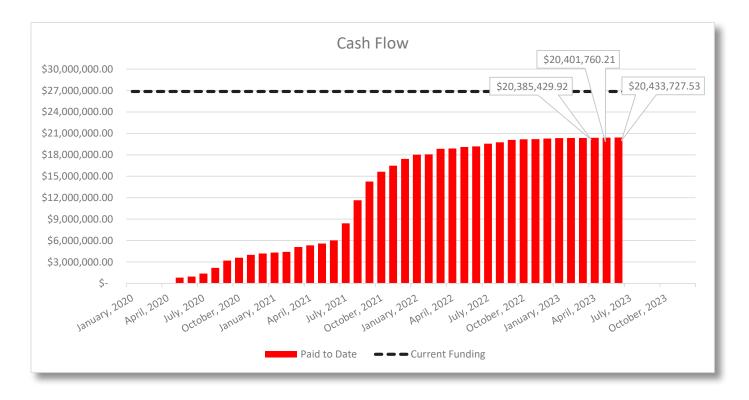

These projects across the District will roll out in phases and include safety, life cycle replacement of building systems, energy efficiency upgrades, accessibility improvements and renovations. The following will provide updates for each of these projects.

19039.018 - Security Upgrades at Trillium Creek Primary School **Project Status:**

This project includes creating a secure entry vestibule and improved classroom lockdown capability.

Recent Activities:

- Office has been cleared and ready for work
- Electrical rough-in for the new security system is underway

Upcoming Activities:

- Demolition and construction of the secure entry vestibule
- Installation of school side door hardware upgrade and classroom security curtains



19059.009 - Security Upgrades at Meridian Creek Middle, Sunset Primary and West Linn High Schools **Project Status:**

This project includes security curtains and improved classroom lockdown capabilities at these three schools.

Recent Activities:

Project window film installation has begun

Upcoming Activities:

Installation of classroom security curtains to start in the coming weeks at all three schools
